



REES ENGINEERING SERVICES LTD.

A Division of Rees NDT Inspection Services Ltd

15612-89 Street
Grande Prairie, Alberta T8V 2N8
engineering@reesndt.com
Phone 780 539 3597
Fax 780 532 8047

16-AUG-2022


PROJECT # RE22-033
WO # 200356

Pathmaker Services Co. Ltd
#100 9215 154 Avenue
Grande Prairie, AB T8X 0L2
CANADA

COMPLIANCE CERTIFICATE

ITEM : CASING ELEVATOR
MAKE : JIANGSU RUTONG PETRO-MACHINERY CO. LTD.
MODEL NO. : TA(DD) 9 5/8 – 150
SERIAL NO. : 200207
CAPACITY : 150 ton

This is to certify that the center latch elevator mention above is in compliance with the API Spec 8C 8.4.7.4.1 PSL1 8.4.7.4.2 based on the document provided by the Manufacturer Jiangsu Rutong Petro-Machinery Co., Ltd.



PERMIT TO PRACTICE	
REES NDT ENGINEERING LTD.	
Signature	<u>ABhatt</u>
Date	<u>16-AUG-2022</u>
PERMIT NUMBER: P 11509	
The Association of Professional Engineers and Geoscientists of Alberta	

ABHAY BHATT, P.Eng

江苏如通石油机械股份有限公司

Jiangsu Rutong Petroleum Machinery Co., Ltd


载荷测试报告

LOAD TEST REPORT

试件描述 Description		套管吊卡 Casing Elevator	试件型号 Type	TA(DD)9 ⁵ / ₈ -150	数量 Qty.	1 付Set
抽样方法 Method of sample		100%	试件数量 Sample Qty.	1	试件编号 Sample No	200207
测试标准 Test std		API Spec 8C	检验类型 Character	出厂检验 Outgoing Inspection	环境温度 Condition	20°C
测试设备 Test equipment	名称 Name	试验台 Electro-hydraulic servo 计算机控制 micro-controlled load device	型号 Type	YEW-10000F	设备编号 Equipment No.	301
	精度 Precision	±1.0%	有效期 Device Certification Expiration Date	2022.8.7	测试日期 Device Test Date	2021.8.8
额定载荷 Load rating		150ton	测试载荷 Test load	225ton	加载时间 Load time	5 mins


测试结果 RESULT

实际测试载荷 Actual test load	225ton(2025kN)	加载时间 Load-Time
----------------------------	----------------	-------------------

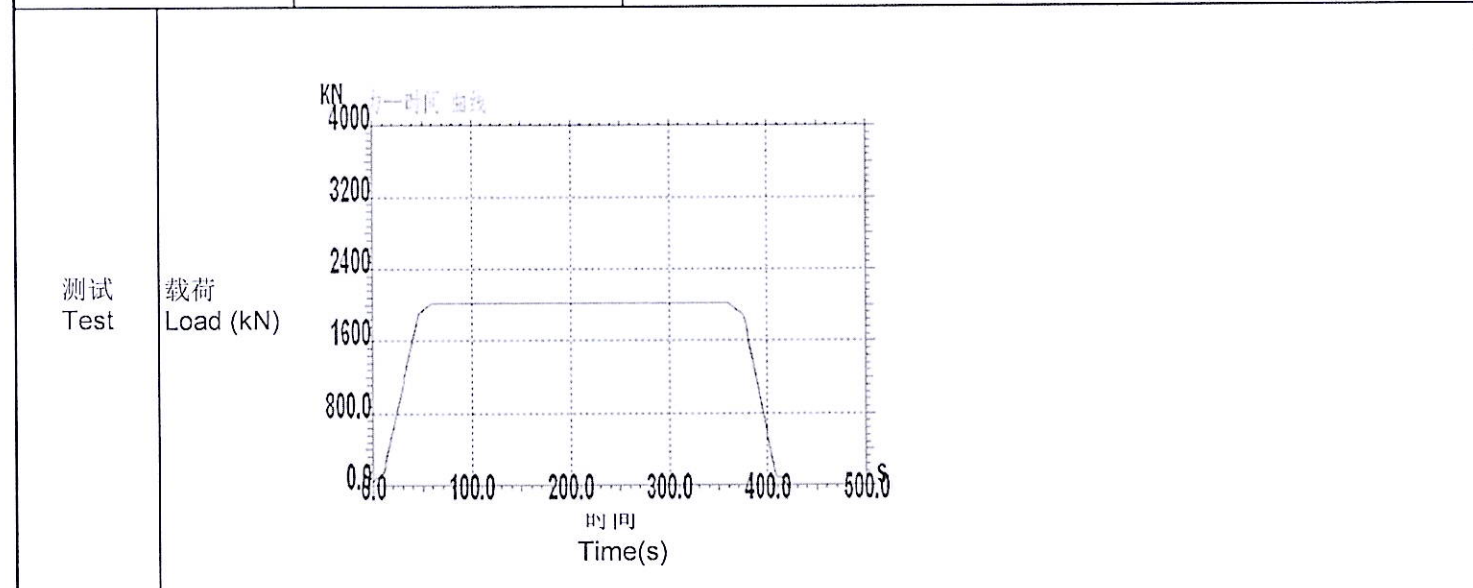

测试结果 TEST RESULT:

合格 Pass

备注 Remark		
--------------	--	---
